


Chinook Care Centre PHASE-2 IMPACT CALENDAR for Feb-23 – March-14 / 2020

Sun	Monday	Tuesday	Wednesday	Thursday	Friday	Sat
Feb-23	Feb-24 <i>C</i>	Feb-25 <i>C</i>	Feb-26 <i>C</i>	Feb-27 <i>C</i>	Feb-28 <i>C</i>	Feb-29
W k 51	➤ South-End Basement Floor Pour After Prep Work Complete ➤ Main Floor South-End Metal Decking inc Plumbing & Electrical RI's ➤ Structural Steel Erection ➤ Finish-Up Foundation Detail & Misc Work					
Mar-1	March-2 <i>C</i>	March-3 <i>C</i>	March-4 <i>C</i>	March-5 <i>C</i>	March-6 <i>C</i>	Mar-7
W k 52	➤ South-End Metal Decking Main Floor Pour After Prep Work Complete ➤ Main Floor Middle Metal Decking inc Plumbing & Electrical RI's ➤ Structural Steel Erection ➤ Finish-Up Foundation Detail & Misc Work					
Mar-8	March-9 <i>C</i>	March-10 <i>C</i>	March-11 <i>C</i>	March-12 <i>C</i>	March-13 <i>C</i>	Mar-14
W k 53	➤ North-End Basement Floor Prep – M&E Ground Works, Gravel Base, ➤ Main Floor Middle Metal Decking inc Plumbing & Electrical RI's ➤ Structural Steel Erection					

IMPACT EVENTS

- | | |
|--|---------------------------------------|
| <i>P</i> Parkade Access Disruptions | <i>S</i> Staff Area Disruptions |
| <i>A</i> Building Access Interruptions | <i>E</i> Planned Electrical Shut Down |
| <i>C</i> Construction Activity | <i>W</i> Planned Water Shut Down |
| <i>R</i> Resident Area Disruptions | <i>N</i> Excess Noise |

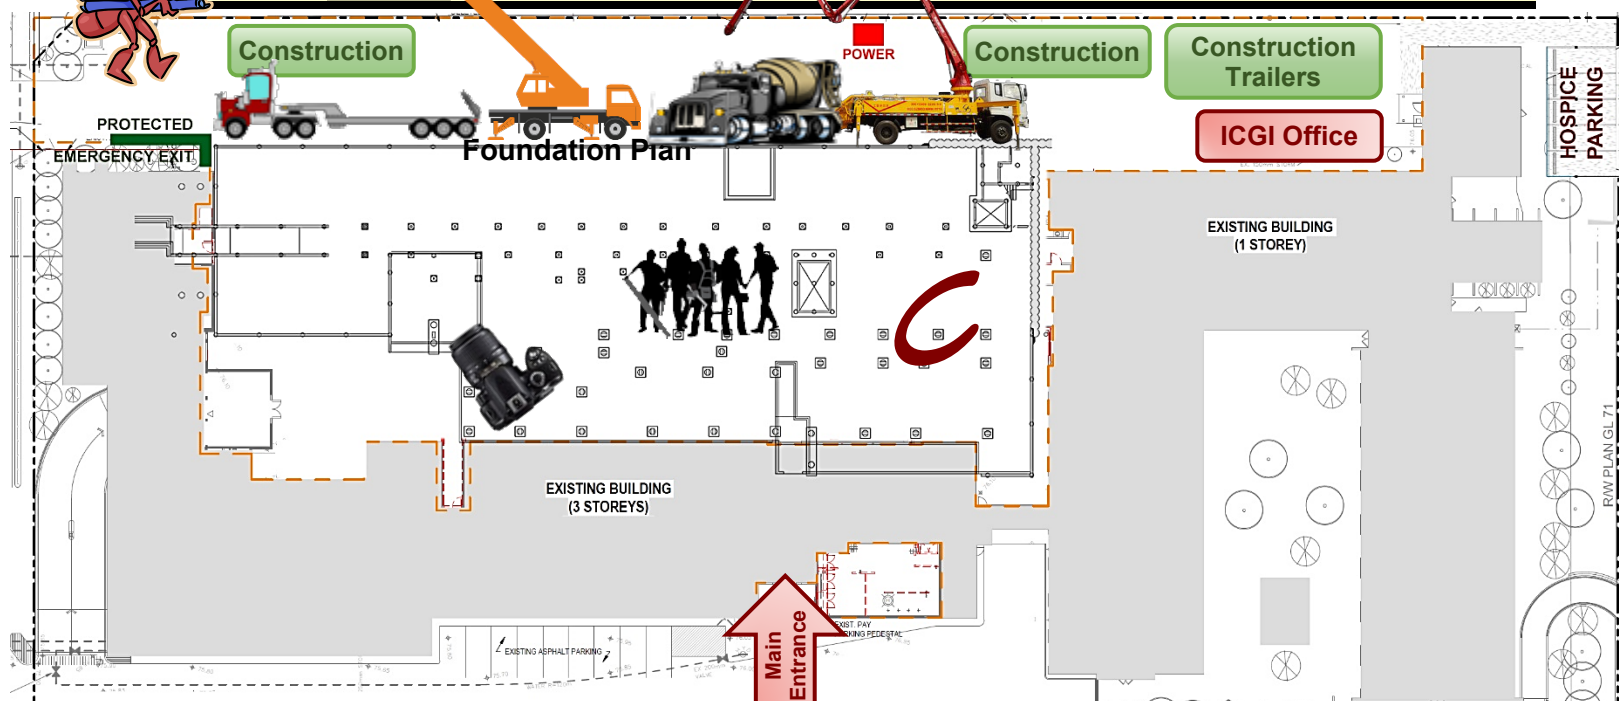

Feb-19/2020

1st Basement Floor Pour
Emergency Generator Room

