


Chinook Care Centre PHASE-2 IMPACT CALENDAR for July-12 – Aug-1 / 2020

Sun	Monday	Tuesday	Wednesday	Thursday	Friday	Sat
July-12	July-13 <i>CR</i>	July-14 <i>CR</i>	July-15 <i>CR</i>	July-16 <i>CR</i>	July-17 <i>CR</i>	July-18
W k 71	<p>➤ Construct Connection Point Barrier Walls Inside Existing Building</p> <p>➤ Roof North-End Mansard & Parapet Framing ➤ Roof South-End Pads & Finishes</p> <p>➤ Ext & Int Wall Framing ➤ Early-Stage Drywalling ➤ Mech & Elect Rough-In's</p>					
July-19	July-20 <i>CR</i>	July-21 <i>CR</i>	July-22 <i>CR</i>	July-23 <i>CR</i>	July-24 <i>CR</i>	July-25
W k 72	<p>➤ Construct Connection Point Barrier Walls Inside Existing Building</p> <p>➤ Roof North-End Insulation & Membrane ➤ Roof South-End Pads & Finishes</p> <p>➤ Ext & Int Wall Framing ➤ Early-Stage Drywalling ➤ Mech & Elect Rough-In's</p>					
July-26	July-27 <i>C</i>	July-28 <i>C</i>	July-29 <i>C</i>	July-30 <i>C</i>	July-31 <i>C</i>	Aug-1
W k 73	<p>➤ Connection Point Construction</p> <p>➤ Roof North-End Insulation & Membrane ➤ Roof South-End Pads & Finishes</p> <p>➤ Ext & Int Wall Framing ➤ Early-Stage Drywalling ➤ Mech & Elect Rough-In's</p>					



IMPACT EVENTS

- P* Parkade Access Disruptions
- A* Building Access Interruptions
- C* Construction Activity
- R* Resident Area Disruptions
- S* Staff Area Disruptions
- E* Planned Electrical Shut Down
- W* Planned Water Shut Down
- N* Excess Noise

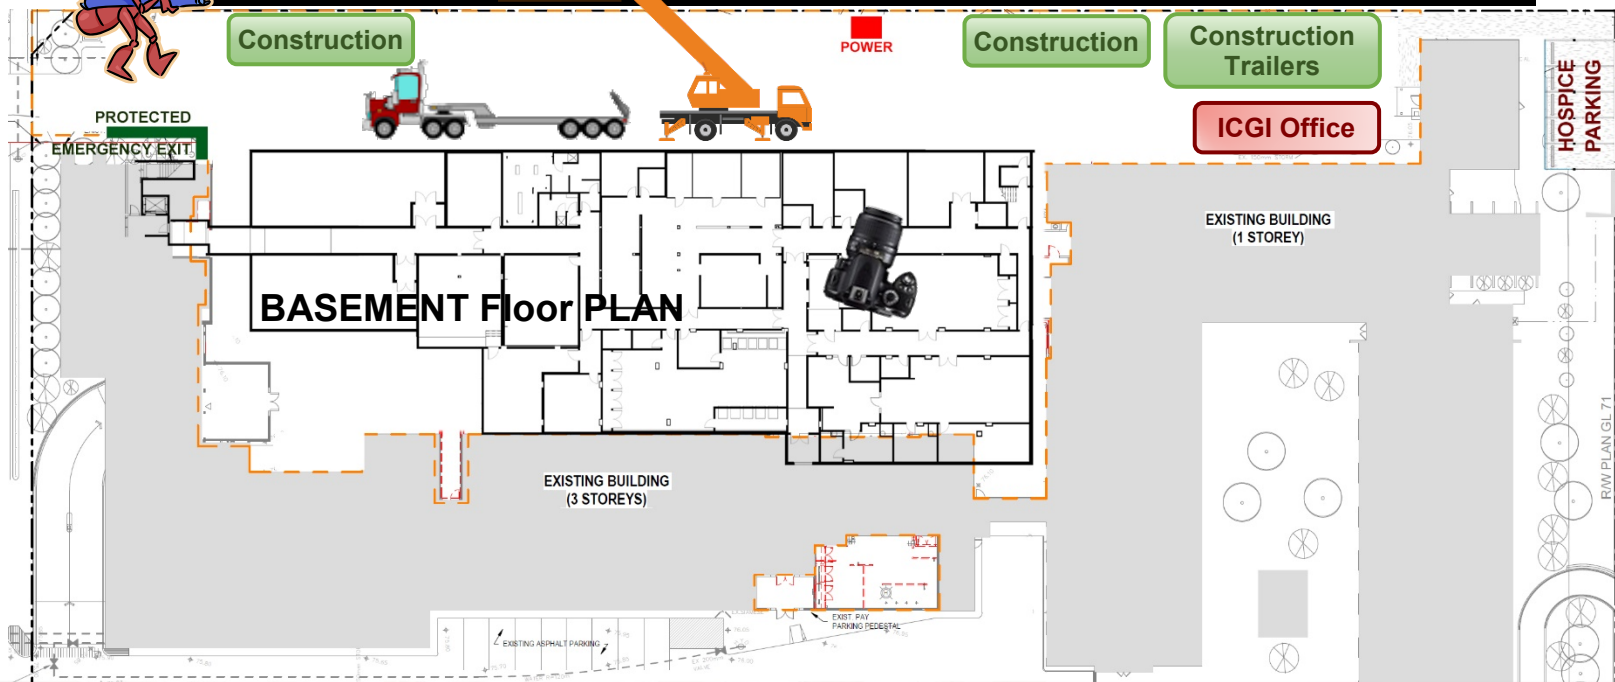

July-8
Fitting-Out The Electrical Room

